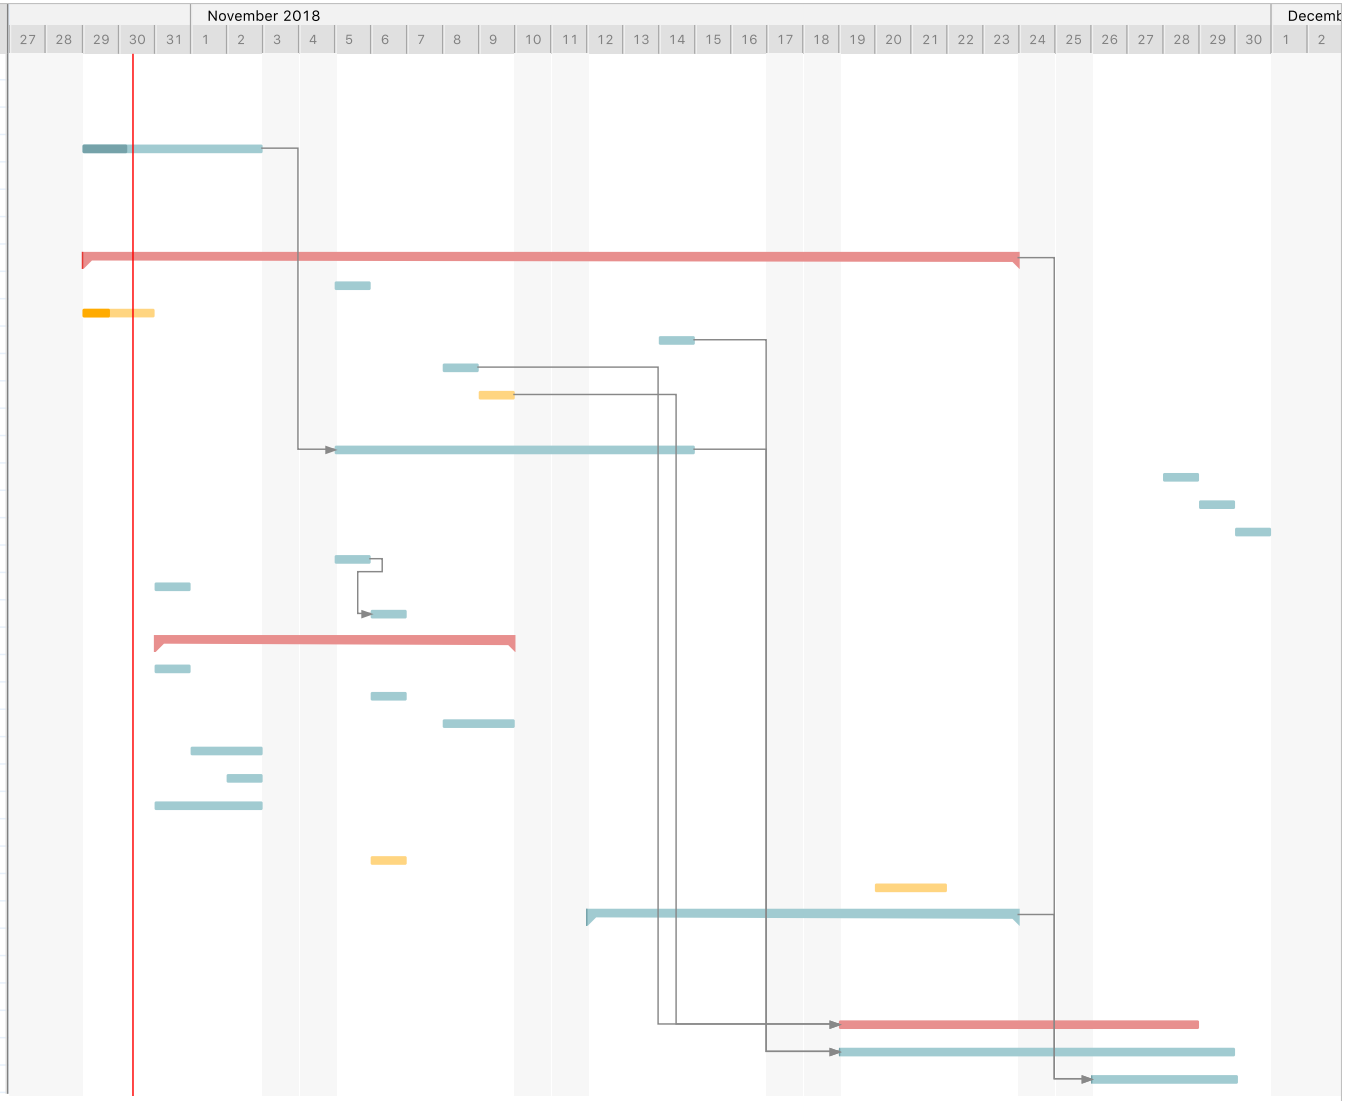	Start	End	Assignee	Priority	Progress
V.V.P. MVP 4/12/'18					
Kickoff					38%
Sitemap - MVP					
Design alignment and appr...	Oct 29, 2018	Nov 3, 2018		5	25%
MVP Scope					
Internal & External planning					
Functional and technical sp...					
Development	Oct 29, 2018	Nov 24, 2018		1	0%
Kickoff meeting	Nov 5, 2018	Nov 6, 2018		5	
Setup	Oct 29, 2018	Oct 31, 2018		2	38%
Permissions	Nov 14, 2018	Nov 15, 2018		5	
Deployment scripts + stagi...	Nov 8, 2018	Nov 9, 2018		5	
Content examples	Nov 9, 2018	Nov 10, 2018		2	
General template structure				5	
Front-end	Nov 5, 2018	Nov 15, 2018		5	
SEO redirects	Nov 28, 2018	Nov 29, 2018		5	
Google Tag Manager (default	Nov 29, 2018	Nov 30, 2018		5	
GDPR	Nov 30, 2018	Dec 1, 2018		5	
Mailchimp	Nov 5, 2018	Nov 6, 2018		5	
Header	Oct 31, 2018	Nov 1, 2018		5	
Footer	Nov 6, 2018	Nov 7, 2018		5	
Content types	Oct 31, 2018	Nov 10, 2018		1	
Home page CT	Oct 31, 2018	Nov 1, 2018		5	
Contact	Nov 6, 2018	Nov 7, 2018		5	
Basic page CT	Nov 8, 2018	Nov 10, 2018		5	
Category	Nov 1, 2018	Nov 3, 2018		5	
News	Nov 2, 2018	Nov 3, 2018		5	
Components	Oct 31, 2018	Nov 3, 2018		5	
Soft elements					
Holiday 1: public holiday	Nov 6, 2018	Nov 7, 2018		2	
Holiday 2: 20/11 + 21/11	Nov 20, 2018	Nov 22, 2018		2	
Testing	Nov 12, 2018	Nov 24, 2018		5	0%
Quality tests by Lead Deve...					
Functional tests by PM					
Source code updates					
Content filling	Nov 19, 2018	Nov 29, 2018		1	
Acceptance	Nov 19, 2018	Nov 30, 2018		5	0%
Deployment	Nov 26, 2018	Nov 30, 2018		5	0%
